

VTP SIERRA PROJECT

Site Progress report

REPORT DATE: 05-08-2025

Building Work Status

Tower	Construction Status
	as on 04.08.2025
TOWER 1	Tower 01 : RCC Completed Gypsum Work - Completed. Waterproofing & Plumbing Work - Completed Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed Flooring Works - Completed Wooden Door Installation - 100% completed Window Installation – 100% completed Glass Railing Installation – 100% Completed (Except First Floor) External Painting – 95% Completed Internal Painting First Coat – 100% Completed Lift Installation Work- Installation Done For All 4 lifts
TOWER 2	Tower 02 : RCC Completed. Gypsum Work - Completed. Waterproofing & Plumbing - Completed. Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed. Flooring Works - Completed. Wooden Door - 20th To 25th Floor WIP Aluminium Works (Window & Door) WIP External Painting Work in progress Internal Painting Works - 12th Floor WIP (1st coat) Lift Installation Work in Progress

Building Work Status

Tower	Construction Status
	as on 04.08.2025
TOWER 3	Above Terrace Activities - Completed Gypsum Work - 26th Floor WIP Waterproofing & Plumbing Work – 26F Floor WIP Fire Fighting Works - 26th Floor WIP. Tiling Works (Toilet Dado) - 22th Floor Work in Progress Flooring Works – 14th Floor WIP
TOWER 4	17th Floor Slab RCC Work - RCC WIP 16th Floor Slab RCC Work - RCC casting completed Gypsum Works - 6th & 7th Floor WIP. Waterproofing Works - 5th & 6th Floor WIP
TOWER 5	19th Floor Slab - RCC WIP 18th Floor Slab - RCC casting completed Gypsum Works - 2nd & 3rd Floor WIP Plumbing Works - 6th, 7th & 8th Floor WIP Waterproofing Works - 6th,7th & 8th Floor WIP
TOWER 6	21st Floor Slab - RCC Casting Completed 22nd Floor Slab- WIP Gypsum Work - 11th & 12th Floor WIP Waterproofing & Plumbing Works - 13th & 14th Floor WIP Fire Fighting Works - 11th Floor WIP Tile Dado - 6th & 7th Floor WIP Kitchen Platform - 5rd Floor WIP Flooring Works - 1st floor WIP
Central Podium	5th Slab RCC Work - RCC Completed Club House 2nd Slab – Completed Finishing Work – 5% Completed Landscape Pardi RCC WIP

Tower 1 – RCC Completed.




Tower 1 – Finishing Work



Tower 2: RCC Completed.




Tower 2 – Finishing Work

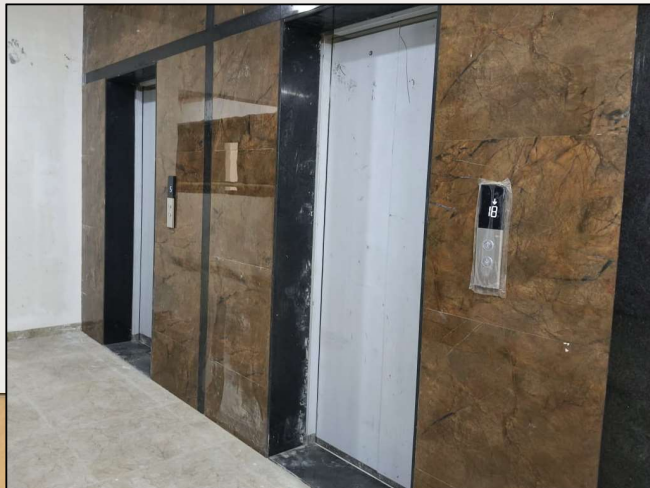

Tower 3 - Above Terrace RCC & Finishing Activities - WIP



Tower 3 – Finishing Work

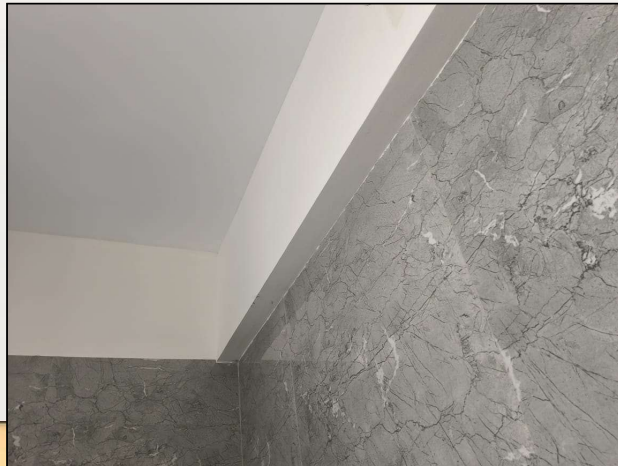

Tower 4 – 17th Floor Slab RCC Work – P1 Completed & P2 WIP.



Tower 5 – 19th Floor Slab – RCC WIP.



Tower 6 – 22nd Floor Slab - RCC WIP
Central Podium – 5th Slab Work Completed



Tower 06

Central Podium

Tower 6 – Finishing Work

