

VTP SIERRA PROJECT

Site Progress report

REPORT DATE: 06-01-2026

Building Work Status

Tower	Construction Status as on 03.01.2026
TOWER 1	Tower 01 : RCC Completed Gypsum Work - Completed. Waterproofing & Plumbing Work - Completed Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed Flooring Works - Completed Wooden Door - Completed, Accessories installation WIP Aluminium Works (Window & Door) - Installation Completed External Painting Completed Internal Painting Works - 26F Completed - 2nd Coat (Final) Paint - Completed Lift Installation Work in Progress (4/4 - Handover Done) Fit-Out Possession - 96%
TOWER 2	Tower 02 : RCC Completed. Gypsum Work - Completed. Waterproofing & Plumbing - Completed. Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed. Flooring Works - Completed. Wooden Door - 26th Floor - Completed, Polishing & Accessories Installation - WIP Aluminium Works (Window & Door) - Installation Completed (HOTO: 15-26F WIP) External Painting Work in progress Internal Painting Works – up to 2nd Coat Paint (1-26F Completed) Lift Installation Work in Progress (4/4 - Handover Done) Fit-Out Possession - 55%
TOWER 3	Gypsum Work - 26th Floor Completed Waterproofing & Plumbing Work - 26F Floor Completed Fire Fighting Works - 26F Floor Completed. Tiling Works (Toilet Dado) - 26th Floor Work in Progress Flooring Works –25th & 26th Floor WIP External Painting Works 96% Completed Aluminium Works (Frame Installation) - 26F Floor Completed Aluminium Work (Shutter Installation) – 20-26F Floor WIP Wooden Door Works – 15-26F Floor WIP Internal Painting Works – 20-26F WIP – Up to 1st Coat paint - 6F WIP. Lift Installation Work in Progress

Building Work Status

TOWER 4

Terrace Floor Slab (31st Slab) RCC Work – P1 RCC Completed & P2 RCC WIP.
 26th Floor Slab (30th Slab) RCC Work - RCC Completed
 Gypsum Works - 15th, 16th & 17th Floor WIP.
 Fire Fighting - 16th, 17th & 18th Floor WIP.
 Plumbing Works - 17th & 18th Floor WIP.
 Waterproofing Works - 16th & 17th Floor WIP
 Flat Flooring – 11th & 13th Work in progress
 T. Dado - 9th Floor Completed, 10th & 11th WIP
 K. Platform - 8th Floor Completed, 9th, 11th WIP
 Wooden Door (Frames) - 2-9F WIP

TOWER 5

Terrace Floor Slab (31st Slab) - RCC Completed
 26th Floor Slab (30th Slab) - RCC Completed
 Gypsum Works - 14th & 15th Floor WIP
 Plumbing Works - 18th, 19th & 20th Floor WIP
 Firefighting - 15th & 16th floor WIP
 Waterproofing Works - 18th & 19th Floor WIP
 Flat Flooring Works - 12th Floor Completed & 13th Floor WIP
 T. Dado - 12th & 13th Floor WIP
 K. Platform - 13th & 14th Floor WIP
 Aluminum Windows (Frames) - 7th Floor Completed, 8-9F WIP.
 Wooden Door Installation (Frames) – 2-9F completed.

TOWER 6

Terrace Floor Slab (31st Slab) – RCC Completed
 Above Terrace RCC works in progress.
 Gypsum Work - 21st, 22nd & 23rd Floor WIP
 Waterproofing & Plumbing Works - 21st & 22nd Floor WIP
 Fire Fighting Works - 23rd Floor WIP
 Tile Dado - 17th & 18th Floor WIP
 Kitchen Platform - 17th & 18th Floor WIP
 Flooring Works - 17th & 18th floor WIP
 Aluminum Windows (Frames) - 16th Floor Completed, 17th Floor WIP
 Wooden Door Installation (Frames) – 2-9F completed


Tower 1 – HOTO in Progress



Tower 01-02 : Night View.




Tower 1 – Finishing Work

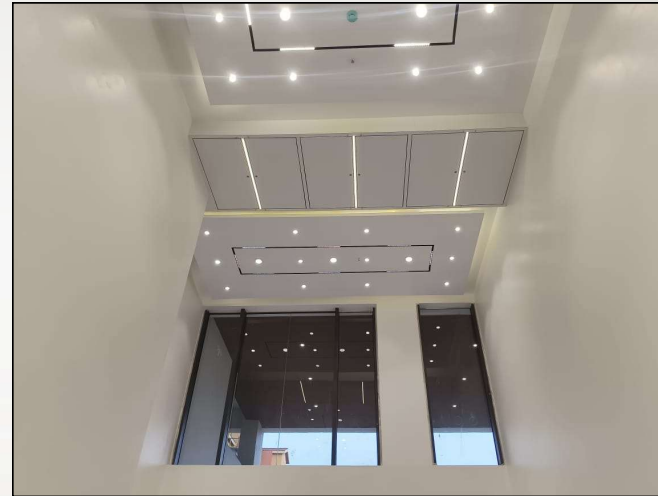

Tower 2: RCC Completed.



Tower 2 – Finishing Work

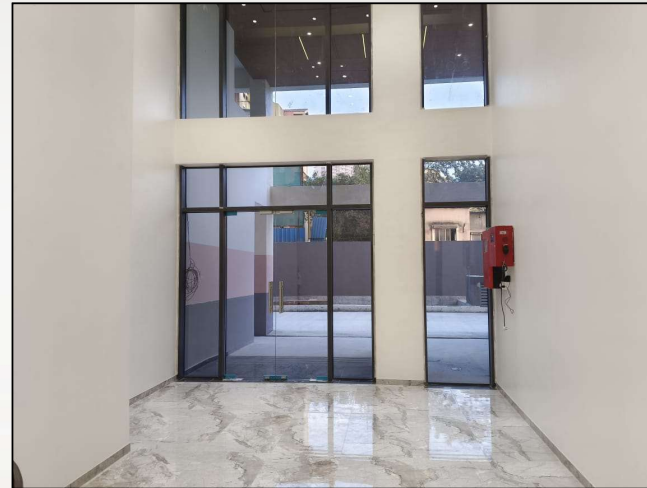

Tower 3 Finishing Activities - WIP




Tower 3 – Finishing Work



Tower 4 – 26th Floor Slab RCC Work – P1 RCC Completed & P2 RCC WIP.



Tower 4 – Finishing Work

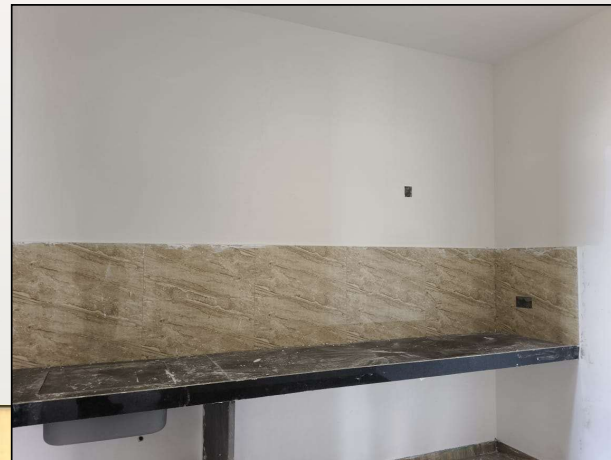

Tower 5 – Terrace Floor Slab – RCC Completed.



Tower 5 – Finishing Work



Tower 6 – Above Terrace Floor RCC WIP Central Podium – 5th Slab Work Completed



Tower 06

Central Podium

Tower 6 – Finishing Work

