

VTP SIERRA PROJECT

Site Progress report

REPORT DATE: 03-02-2026

Building Work Status

Project / Township	Tower	Construction Status
		as on 03.02.2026
SIERRA	TOWER 1	Tower 01 : RCC Completed Gypsum Work - Completed. Waterproofing & Plumbing Work - Completed Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed Flooring Works - Completed Wooden Door - Completed, Accessories installation WIP Aluminium Works (Window & Door) - Installation Completed External Painting Completed Internal Painting Works - 26F Completed - 2nd Coat (Final) Paint - Completed Lift Installation - (Handover Done)
SIERRA	TOWER 2	Tower 02 : RCC Completed. Gypsum Work - Completed. Waterproofing & Plumbing - Completed. Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed. Flooring Works - Completed. Wooden Door - 26th Floor - Completed, Polishing & Accessories Installation - WIP Aluminium Works (Window & Door) - Installation Completed (HOTO: 15-26F WIP) External Painting Work in progress Internal Painting Works – up to 2nd Coat Paint (1-26F Completed) Lift Installation - (Handover Done)
SIERRA	TOWER 3	Gypsum Work - 26th Floor Completed Waterproofing & Plumbing Work - 26F Floor Completed Fire Fighting Works - 26F Floor Completed. Tiling Works (Toilet Dado) - 26th Floor Work in Progress Flooring Works –26th Floor WIP External Painting Works WIP Aluminium Works (Accessories Installation) - WIP Aluminium Work (Shutter Installation) – 26F Floor Completed; Wooden Door Works – 22-26F Floor WIP Internal Painting Works – 20-26F WIP – Up to 1st Coat paint - 15F WIP. Lift Installation - S1/F1 Completed; P1/P2 - WIP

Building Work Status

SIERRA	TOWER 4	Above Terrace Activities WIP Terrace Floor Slab (31st Slab) RCC Work - RCC Completed. Gypsum Works - 19th & 20th Floor WIP. Fire Fighting - 17th & 18th Floor WIP. Plumbing Works - 17th, 18th & 19th Floor WIP. Waterproofing Works - 19th & 20th Floor WIP Flat Flooring – 13th, 14th & 15th Work in progress T. Dado - 13th Floor Completed, 14th & 15th WIP K. Platform - 14th Floor Completed, 15th, 16th WIP Wooden Door (Frames) - 14F & 15F WIP (M.D & B.D)
SIERRA	TOWER 5	Terrace Floor Slab (31st Slab) - RCC Completed Above Terrace Activities WIP. Gypsum Works - 19th & 20th Floor WIP Plumbing Works - 20th, 21st & 22nd Floor WIP Firefighting - 16th & 17th floor WIP Waterproofing Works - 19th & 20th Floor WIP Flat Flooring Works - 12th Floor Completed & 13th & 14th Floor WIP T. Dado - 13th & 14th Floor WIP K. Platform - 13th & 14th Floor WIP Aluminum Windows (Frames) - 12th Floor Completed, 13-15F WIP. Wooden Door Installation (Frames) – 11F completed; 12F WIP
SIERRA	TOWER 6	Above Terrace Activities WIP Terrace Floor Slab (31st Slab) – RCC Completed Gypsum Work - 22nd, 23rd & 24th Floor WIP Waterproofing & Plumbing Works - 21st, 22nd & 23rd Floor WIP Fire Fighting Works - 23rd & 24th Floor WIP Tile Dado - 21st & 22nd Floor WIP Kitchen Platform - 20th & 21st Floor WIP Flooring Works - 19th & 20th floor WIP Aluminum Windows (Frames) - 20th Floor Completed, 21st & 22nd Floor WIP Wooden Door Installation (Frames) – 17F (M.D) completed.

Tower 1 – RCC Completed.



Tower 01-02 : Night View.



Tower 1 – Finishing Work



Tower 2: RCC Completed.




Tower 2 – Finishing Work



Tower 3 Finishing Activities - WIP



Tower 3 – Finishing Work

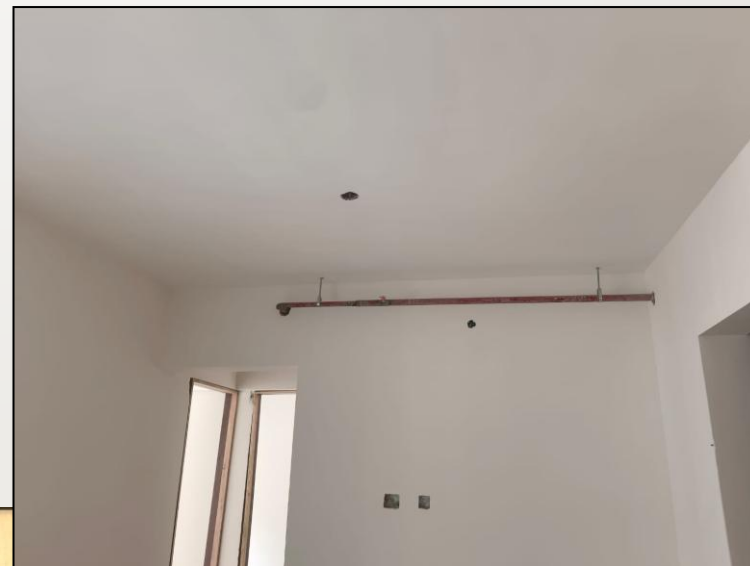

Tower 4 – Terrace Floor Slab RCC Work Completed; AT Work WIP



Tower 4 – Finishing Work



Tower 5 – Terrace Floor Slab RCC Work Completed; AT Work WIP



Tower 5 – Finishing Work



Tower 6 – Terrace Floor Slab RCC Work Completed; AT Work WIP Central Podium – 5th Slab Work Completed



Central Podium

Tower 6 – Finishing Work

