

# VTP SIERRA PROJECT

## Site Progress report

REPORT DATE: 05-03-2026

# Building Work Status

| Project / Township | Tower   | Construction Status                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  |
|--------------------|---------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                    |         | as on 05.03.2026                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     |
| SIERRA             | TOWER 1 | <p>Tower 01 : RCC Completed.<br/> Gypsum Work - Completed.<br/> Waterproofing &amp; Plumbing Work - Completed.<br/> Fire Fighting Work - Completed.<br/> Tiling Works (Toilet Dado) - Completed.<br/> Flooring Works - Completed.<br/> Wooden Door - Completed, Accessories installation WIP.<br/> Aluminium Works (Window &amp; Door) - Installation Completed.<br/> External Painting Completed.<br/> Internal Painting Works - 26F Completed - 2nd Coat (Final) Paint - Completed.<br/> Lift Installation - (F1, S1, P1 &amp; P2 - Handover Done).</p>                                            |
| SIERRA             | TOWER 2 | <p>Tower 02 : RCC Completed.<br/> Gypsum Work - Completed.<br/> Waterproofing &amp; Plumbing - Completed.<br/> Fire Fighting Work - Completed.<br/> Tiling Works (Toilet Dado) - Completed.<br/> Flooring Works - Completed.<br/> Wooden Door - 26th Floor - Completed, Polishing &amp; Accessories Installation - WIP.<br/> Aluminium Works (Window &amp; Door) - Installation Completed (HOTO: 15-26F WIP).<br/> Internal Painting Works – up to 2nd Coat Paint (1-26F Completed).<br/> Lift Installation - (F1, S1, P1 &amp; P2 - Handover Done).</p>                                             |
| SIERRA             | TOWER 3 | <p>Gypsum Work - 26th Floor Completed.<br/> Waterproofing &amp; Plumbing Work - 26F Floor Completed.<br/> Fire Fighting Works - 26F Floor Completed.<br/> Tiling Works (Toilet Dado) - 26th Floor Completed.<br/> Flooring Works –26th Floor Completed.<br/> External Painting Works WIP.<br/> Aluminium Works (Accessories Installation) - WIP.<br/> Aluminium Work (Shutter Installation) – 26F Floor Completed.<br/> Wooden Door Works – 23-26F Floor WIP.<br/> Internal Painting Works – 21-26F WIP – Up to 1st Coat paint - 15F WIP.<br/> Lift Installation - S1,F1, P1 &amp; P2 Completed.</p> |

# Building Work Status

| Project / Township | Tower   | Construction Status                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  |
|--------------------|---------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                    |         | as on 05.03.2026                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     |
| SIERRA             | TOWER 4 | <p>Terrace Floor Slab (31st Slab) RCC Work - Completed.</p> <p>Above Terrace Activities WIP.</p> <p>Gypsum Works - 21<sup>st</sup>, 22<sup>nd</sup> &amp; 23<sup>rd</sup> Floor WIP.</p> <p>Fire Fighting - 22nd, 23rd &amp; 24thth Floor WIP.</p> <p>Plumbing Works - 19th, 20th &amp; 21st Floor WIP.</p> <p>Waterproofing Works - 19th, 20th &amp; 21st Floor WIP.</p> <p>Flat Flooring – 16<sup>th</sup>, 17<sup>th</sup> &amp; 18<sup>th</sup> Work in progress.</p> <p>T. Dado - 15th Floor Completed, 16th &amp; 17th WIP.</p> <p>K. Platform - 18th Floor Completed, 19th, 20th WIP.</p> <p>Alu. Win (Frame) - 12-20F WIP.</p> <p>Wooden Door (Frames) - 15F &amp; 16F WIP (M.D &amp; B.D).</p>                              |
| SIERRA             | TOWER 5 | <p>Terrace Floor Slab (31st Slab) - Completed.</p> <p>Above Terrace Activities WIP.</p> <p>Gypsum Works - 21<sup>st</sup>, 22<sup>nd</sup> &amp; 23<sup>rd</sup> Floor WIP.</p> <p>Plumbing Works - 21st, 22nd &amp; 23rd Floor WIP.</p> <p>Firefighting - 20th, 21st &amp; 22nd floor WIP.</p> <p>Waterproofing Works - 21<sup>st</sup>, 22<sup>nd</sup> &amp; 23<sup>rd</sup> Floor WIP.</p> <p>Flat Flooring Works - 13th Floor Completed &amp; 14th, 15th &amp; 16th Floor WIP.</p> <p>T. Dado - 14th, 15th &amp; 16th Floor WIP.</p> <p>K. Platform - 15th &amp; 16th Floor WIP.</p> <p>Aluminum Windows (Frames) - 13th Floor Completed, 14-16F WIP.</p> <p>Wooden Door Installation (Frames) – 11F completed; 12-15F WIP.</p> |
| SIERRA             | TOWER 6 | <p>Terrace Floor Slab (31st Slab) – Completed.</p> <p>Above Terrace Activities WIP.</p> <p>Gypsum Work - 23rd, 24th &amp; 25th Floor WIP.</p> <p>Waterproofing &amp; Plumbing Works - 23rd &amp; 24th Floor WIP.</p> <p>Fire Fighting Works - 23rd &amp; 24th Floor WIP.</p> <p>Tile Dado - 22nd &amp; 23rd Floor WIP.</p> <p>Kitchen Platform - 22nd &amp; 23rd Floor WIP.</p> <p>Flooring Works - 20th &amp; 21st floor WIP.</p> <p>Aluminum Windows (Frames) – 22<sup>nd</sup> Floor Completed, 23<sup>rd</sup> &amp; 24<sup>th</sup> Floor WIP.</p> <p>Wooden Door Installation (Frames) – 17-20F (M.D) completed.</p>                                                                                                           |

# Tower 1 – RCC Completed.






## Tower 01-02 : Night View.



# Tower 1 – Finishing Work

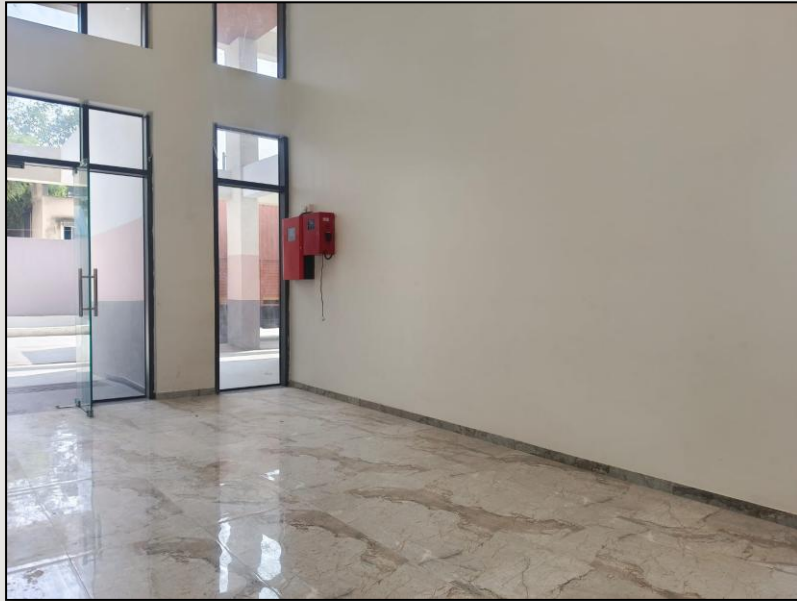



# Tower 2: RCC Completed.



# Tower 2 – Finishing Work





# Tower 3 Finishing Activities - WIP



# Tower 3 – Finishing Work





## Tower 4 – Terrace Floor Slab RCC Work Completed; AT Work WIP





# Tower 4 – Finishing Work




## Tower 5 – Terrace Floor Slab RCC Work Completed; AT Work WIP





# Tower 5 – Finishing Work

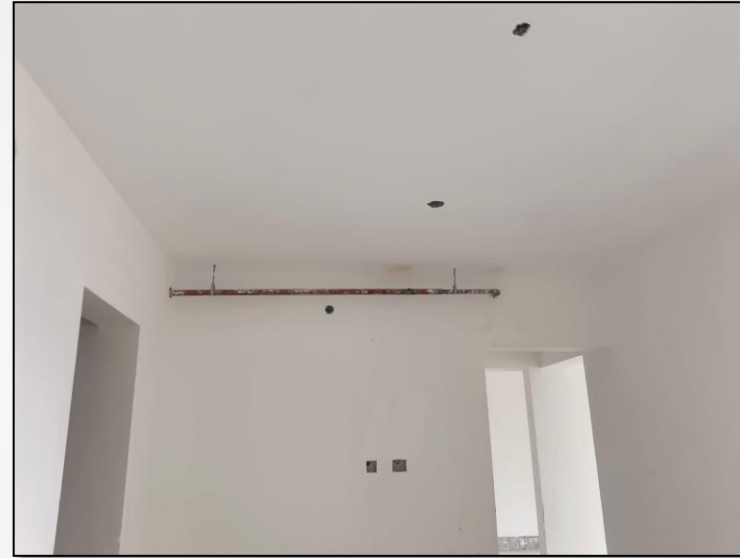

# Tower 6 – Terrace Floor Slab RCC Work Completed; AT Work WIP Central Podium – 5<sup>th</sup> Slab Work Completed



Central Podium



# Tower 6 – Finishing Work

