

VTP SIERRA PROJECT

Site Progress report

REPORT DATE: 05-04-2026

Building Work Status

Tower	Construction Status
	as on 30.03.2026
TOWER 1	Tower 01 : RCC Completed. Gypsum Work - Completed. Waterproofing & Plumbing Work - Completed. Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed. Flooring Works - Completed. Wooden Door - Completed, Accessories installation WIP. Aluminium Works (Window & Door) - Installation Completed. External Painting Completed. Internal Painting Works - 26F Completed - 2nd Coat (Final) Paint - Completed. Lift Installation - (F1, S1, P1 & P2 - Handover Done).
TOWER 2	Tower 02 : RCC Completed. Gypsum Work - Completed. Waterproofing & Plumbing - Completed. Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed. Flooring Works - Completed. Wooden Door - 26th Floor - Completed, Polishing & Accessories Installation - WIP. Aluminium Works (Window & Door) - Installation Completed (HOTO: 15-26F WIP). External Painting Work in progress. Internal Painting Works – up to 2nd Coat Paint (1-26F Completed). Lift Installation - (F1, S1, P1 & P2 - Handover Done).
TOWER 3	Gypsum Work - 26th Floor Completed. Waterproofing & Plumbing Work - 26F Floor Completed. Fire Fighting Works - 26F Floor Completed. Tiling Works (Toilet Dado) - 26F Floor Completed. Flooring Works –26F Floor Completed. External Painting Works WIP. Aluminium Work (Shutter Installation) – 26F Floor Completed. Wooden Door Works – 23-26F Floor WIP. Internal Painting Works – 21-26F WIP – Up to 1st Coat paint - 16-26 WIP, 2nd Coat paint - 09-13F WIP Lift Installation - S1,F1, P1 & P2 Completed.

Building Work Status

Tower	Construction Status
	as on 30.03.2026
TOWER 4	Terrace Floor Slab (31st Slab) RCC Work - RCC Completed. Above Terrace Activities WIP. Gypsum Works - 23rd & 24th Floor WIP. Fire Fighting - 23rd & 24thth Floor WIP. Plumbing Works - 22nd & 23rd Floor WIP. Waterproofing Works - 20th & 21st Floor WIP. Flat Flooring – 15th, 16th & 17th Work in progress. T. Dado - 15th Floor Completed, 16th & 17th WIP. K. Platform - 19th Floor Completed, 20th, 21st WIP. Alu. Win (Frame) – 12th-13th WIP. Wooden Door (Frames) - 15F & 16F WIP (M.D & B.D).
TOWER 5	Terrace Floor Slab (31st Slab) - RCC Completed. Above Terrace Activities WIP. Gypsum Works - 24th & 25th Floor WIP. Plumbing Works - 23rd & 24th Floor WIP. Firefighting - 18th & 19th floor WIP. Waterproofing Works - 20th & 21st Floor WIP. Flat Flooring Works - 15th Floor Completed & 16th & 17th Floor WIP. T. Dado - 16th & 17th Floor WIP. K. Platform - 17th & 18th Floor WIP. Aluminum Windows (Frames) - 13th Floor Completed, 14-16F WIP. Wooden Door Installation (Frames) – 13F completed; 14-16F WIP.
TOWER 6	Terrace Floor Slab (31st Slab) – RCC Completed. Above Terrace Activities WIP. Gypsum Work - 25th & 26th Floor WIP. Waterproofing & Plumbing Works - 24th & 25th Floor WIP. Fire Fighting Works - 23rd & 24th Floor WIP. Tile Dado - 23rd & 24th Floor WIP. Kitchen Platform - 23rd & 24th Floor WIP. Flooring Works - 21st & 22nd floor WIP. Aluminum Windows (Frames) - 21st Floor Completed, 22nd & 23rd Floor WIP. Wooden Door Installation (Frames) – 17-20F (M.D) completed.

Tower 1 – RCC Completed.



Tower 01-02 : Night View.



Tower 1 – Finishing Work



Tower 2: RCC Completed.




Tower 2 – Finishing Work



Tower 3 Finishing Activities - WIP




Tower 3 – Finishing Work

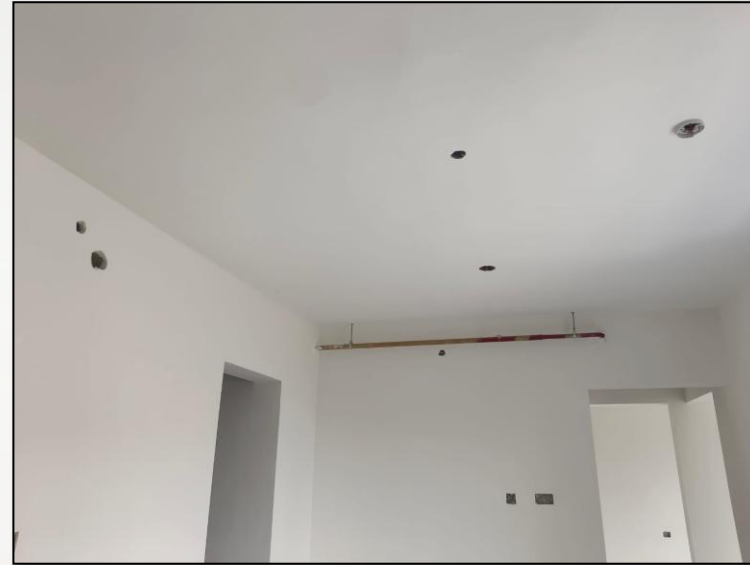

Tower 4 – Terrace Floor Slab RCC Work Completed; Above Terrace Work WIP



Tower 4 – Finishing Work

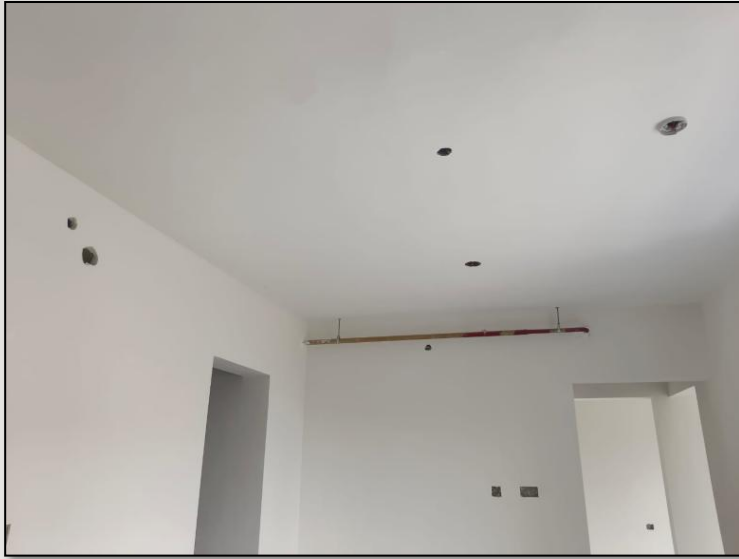

Tower 5 – Terrace Floor Slab RCC Work Completed; AT Work WIP



Tower 5 – Finishing Work



Tower 6 – Terrace Floor Slab RCC Work Completed; AT Work WIP Central Podium – 5th Slab Work Completed



Central Podium

Tower 6 – Finishing Work

