

VTP SIERRA PROJECT

Site Progress report

REPORT DATE: 05-MAY-2026

Building Work Status

Project / Township	Tower	Construction Status
		as on 30.04.2026
SIERRA	TOWER 1	Tower 01 : RCC Completed. Gypsum Work - Completed. Waterproofing & Plumbing Work - Completed. Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed. Flooring Works - Completed. Wooden Door - Completed, Accessories installation WIP. Aluminium Works (Window & Door) - Installation Completed. External Painting Completed. Internal Painting Works - 26F Completed - 2nd Coat (Final) Paint - Completed. Lift Installation - (F1, S1, P1 & P2 - Handover Done).
SIERRA	TOWER 2	Tower 02 : RCC Completed. Gypsum Work - Completed. Waterproofing & Plumbing - Completed. Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed. Flooring Works - Completed. Wooden Door - 26th Floor - Completed, Polishing & Accessories Installation - WIP. Aluminium Works (Window & Door) - Installation Completed (HOTO: 15-26F WIP). External Painting Work in progress. Internal Painting Works – up to 2nd Coat Paint (1-26F Completed). Lift Installation - (F1, S1, P1 & P2 - Handover Done).
SIERRA	TOWER 3	Gypsum Work - 26th Floor Completed. Waterproofing & Plumbing Work - 26F Floor Completed. Fire Fighting Works - 26F Floor Completed. Tiling Works (Toilet Dado) - 26F Floor Completed. Flooring Works –26F Floor Completed. External Painting Works WIP. Aluminium Works (Accessories Installation) - WIP. Aluminium Work (Shutter Installation) – 26F Floor Completed. Wooden Door Works – 23-26F Floor WIP. Internal Painting Works – 21-26F WIP Up to 1st Coat paint - 16-26 WIP, 2nd Coat paint - 12-20F WIP Lift Installation - S1,F1, P1 & P2 Completed.

Building Work Status

Project / Township	Tower	Construction Status
		as on 30.04.2026
SIERRA	TOWER 4	Above Terrace RCC Activities Completed. Gypsum Works - 24th & 25th Floor WIP. Fire Fighting - 23rd & 24th Floor WIP. Plumbing Works - 23rd & 24th Floor WIP. Waterproofing Works - 23rd & 24th Floor WIP. Flat Flooring – 17th, 18th & 19th Work in progress. T. Dado - 16th Floor Completed, 17th & 18th WIP. K. Platform - 20th Floor Completed, 21st & 22nd WIP. Alu. Win (Frame) - 14-15 WIP. Alu. Win (Shutter) - 09-10 WIP. Wooden Door (Frames) - 15F & 16F WIP (M.D & B.D). Wooden Door (Shutter) - 15F & 16F WIP (M.D & B.D). Int. Paint (1st Coat) - 2-10F WIP
SIERRA	TOWER 5	Terrace Floor Slab (31st Slab) - RCC Completed. Above Terrace Activities WIP. Gypsum Works - 25th & 26th Floor WIP. Plumbing Works - 25th & 26th Floor WIP. Firefighting - 15th, 16th & 17th floor WIP. Waterproofing Works - 23rd & 24th Floor WIP. Flat Flooring Works - 17th Floor Completed & 18th & 19th Floor WIP. T. Dado - 18th & 19th Floor WIP. K. Platform - 18th & 19th Floor WIP. Alu. Windows (Frames) - 13th Floor Completed, 14-16F WIP. Alu. Windows (Shutter) - 09th Floor Completed, 10-13F WIP. W. Door Installation (Frames) – 13F completed; 14-16F WIP. W. Door Installation (Shutter) – 11F completed; 12-16F WIP. Int. Paint (1st Coat) - 2-3F WIP
SIERRA	TOWER 6	Above Terrace Activities Completed Gypsum Work – 25th & 26th Floor WIP. Waterproofing & Plumbing Works - 24th to 26th Floor WIP. Fire Fighting Works - 25th & 26th Floor WIP. Tile Dado - 23rd & 24th Floor WIP. Kitchen Platform - 23rd & 24th Floor WIP. Flooring Works – 22nd, 23rd & 24th floor WIP. Alu. Win. (Frames) - 23rd Floor Completed, 24th, 25th & 26th Floor WIP. Alu. Win. (Shutter) - 23rd Floor Completed, 24th, 25th & 26th Floor WIP. W. Door Installation (Frames) – 21-23F (M.D) WIP. W. Door Installation (Shutter) – 16-18F (M.D) WIP. Int. Paint (1st Coat) - 10-15F WIP

Tower 1 – RCC Completed.



Tower 01-02 : Night View.



Tower 1 – Finishing Work



Tower 2: RCC Completed.



Tower 2 – Finishing Work



Tower 3 Finishing Activities - WIP



Tower 3 – Finishing Work



Tower 4 – Above Terrace Work Completed




Tower 4 – Finishing Work



Tower 5 – Terrace Floor Slab RCC Work Completed; AT Work WIP



Tower 5 – Finishing Work

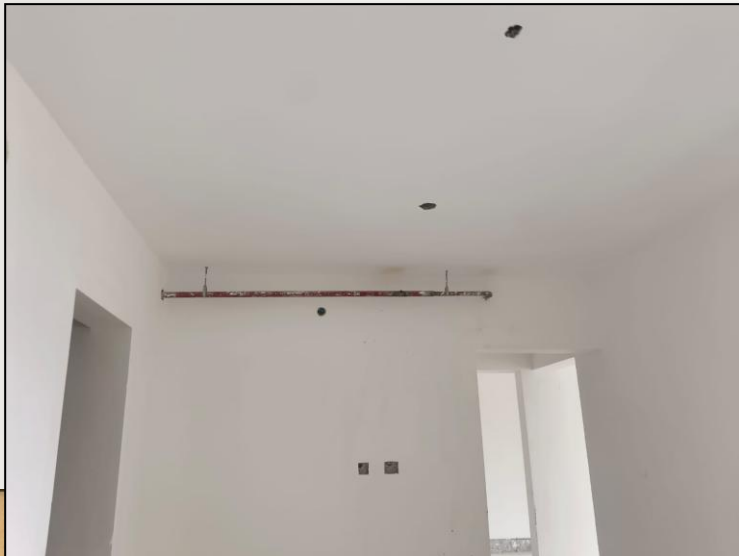

Tower 6 – Terrace Floor Slab RCC Work Completed; AT Work WIP



Tower 6 – Finishing Work



Central Podium – Club House Finishing & Amenities Area WIP



Central Podium



Club House
