

VTP SIERRA PROJECT

Site Progress report

REPORT DATE: 05-12-2025

Building Work Status

Tower	Construction Status as on 30.11.2025
TOWER 1	Tower 01 : RCC Completed Gypsum Work - Completed. Waterproofing & Plumbing Work - Completed Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed Flooring Works - Completed Wooden Door - Completed, Accessories installation – Done, Testing WIP Aluminium Works (Window & Door) - Installation Completed External Painting Completed Internal Painting Works - 26F Completed - 2nd Coat (Final) Paint - Completed Lift Installation Work in Progress (4/4 - Handover Done)
TOWER 2	Tower 02 : RCC Completed. Gypsum Work - Completed. Waterproofing & Plumbing - Completed. Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed. Flooring Works - Completed. Wooden Door - 26th Floor - Completed, Polishing & Accessories Installation - WIP Aluminium Works (Window & Door) - Installation Completed (HOTO: 15-26F WIP) External Painting Work in progress Internal Painting Works – up to 2nd Coat Paint (1-26F Completed) Lift Installation Work in Progress (4/4 - Handover Done)
TOWER 3	Above Terrace Activities - Completed Gypsum Work - 26th Floor Completed Waterproofing & Plumbing Work - 26F Floor Completed Fire Fighting Works - 26F Floor Completed. Tiling Works (Toilet Dado) - 25th & 26th Floor Work in Progress Flooring Works –24th & 25th Floor WIP External Painting Works WIP Aluminium Works (Frame Installation) - 13-26F Floor WIP Aluminium Work (Shutter Installation) – 2-7F Floor WIP Lift Installation Work in Progress

Building Work Status

TOWER 4	25th Floor Slab (29th Slab) RCC Work - RCC Completed. 26th Floor Slab (30th Slab) RCC Work - RCC WIP Gypsum Works - 15th & 16th Floor WIP. Fire Fighting - 14th & 15th Floor WIP. Plumbing Works - 17th & 18th Floor WIP. Waterproofing Works - 15th & 16th Floor WIP Flat Flooring – 4th & 9th Work in progress T. Dado - 8th Floor Completed, 9th & 10th WIP K. Platform - 7th Floor Completed, 4th, 11th WIP
TOWER 5	25th Floor Slab (29th Slab) - RCC Completed 26th Floor Slab (30th Slab) - RCC WIP Gypsum Works - 12th & 13th Floor WIP Plumbing Works - 18th & 19th Floor WIP Firefighting - 15th & 16th floor WIP Waterproofing Works - 18th & 19th Floor WIP Flat Flooring Works - 10th Floor Completed & 11th Floor WIP T. Dado - 11th & 12th Floor WIP K. Platform - 11th & 12th Floor WIP Aluminum Windows (Frames) - 7th Floor Completed, 8-9F WIP.
TOWER 6	26th Floor Slab (30th Slab) - RCC Completed. Terrace Floor Slab (31st Slab) – RCC Completed Gypsum Work - 20th & 21st Floor WIP Waterproofing & Plumbing Works - 20th & 21st Floor WIP Fire Fighting Works - 20th Floor WIP Tile Dado - 15th & 16th Floor WIP Kitchen Platform - 16th & 17th Floor WIP Flooring Works - 15th & 16th floor WIP Aluminum Windows (Frames) - 11th Floor Completed, 12th Floor WIP


Tower 1 – RCC Completed.



Tower 01-02 : Night View.



Tower 1 – Finishing Work

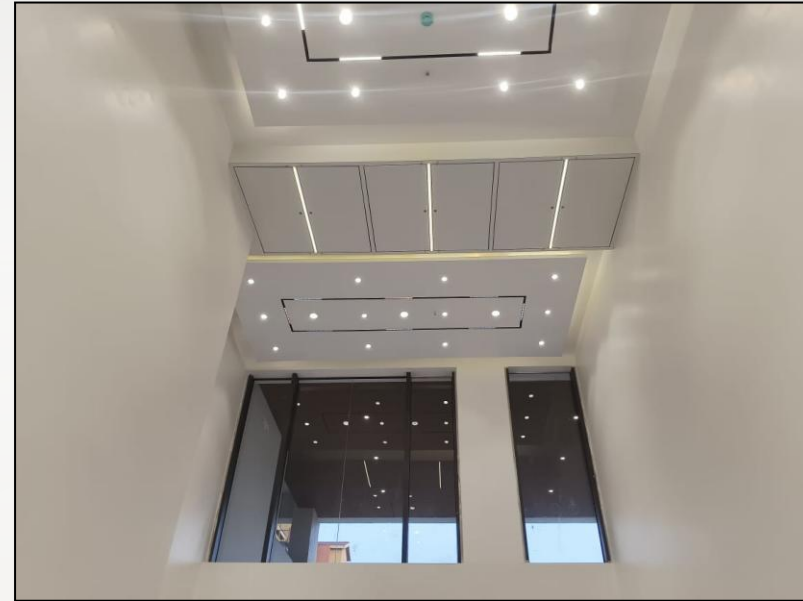

Tower 2: RCC Completed.



Tower 2 – Finishing Work



Tower 3 Finishing Activities - WIP



Tower 3 – Finishing Work



Tower 4 – 25th Floor Slab RCC Work – WIP.



Tower 4 – Finishing Work



Tower 5 – 25th Floor Slab – RCC WIP.



Tower 5 – Finishing Work



Tower 6 – Terrace Floor Slab (31st Slab) – RCC Completed Central Podium – 5th Slab Work Completed



Tower 06

Central Podium

Tower 6 – Finishing Work

