

VTP SIERRA PROJECT

Site Progress report

REPORT DATE: 06-10-2025

Building Work Status

Project / Township	Tower	Construction Status
		as on 30.09.2025
SIERRA	TOWER 1	Tower 01 : RCC Completed Gypsum Work - Completed. Waterproofing & Plumbing Work - Completed Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed Flooring Works - Completed Wooden Door - Completed, Accessories installation WIP Aluminium Works (Window & Door) - Installation Completed External Painting Work - WIP Internal Painting Works - Completed, Second Coat WIP above 22nd floor Lift Installation - Done
SIERRA	TOWER 2	Tower 02 : RCC Completed. Gypsum Work - Completed. Waterproofing & Plumbing - Completed. Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed. Flooring Works - Completed. Wooden Door - 26th Floor - Completed, Polishing & Accessories Installation - WIP Aluminium Works (Window & Door) - Installation WIP External Painting Work in progress Internal Painting Works - 13-26th Floor WIP (1st coat) Lift Installation Work in Progress (2/4 - Handover Done)
SIERRA	TOWER 3	Above Terrace Activities - Completed Gypsum Work - 26th Floor Completed Waterproofing & Plumbing Work - 26th Floor Completed Fire Fighting Works - 26th Floor Completed. Tiling Works (Toilet Dado) - 26th Floor Work in Progress Flooring Works – 17th & 18th Floor WIP External Painting Works WIP Aluminum Works (Frame Installation) - 12th & 13th Floor WIP



Building Work Status

SIERRA	TOWER 4	22nd Floor Slab (26th Slab) RCC Work - RCC WIP 21st Floor Slab (25th Slab) RCC Work - RCC Completed Gypsum Works - 11th & 12th Floor WIP. FireFighting - 8th-9th Floors WIP Plumbing Works - 9th & 10th Floor WIP Waterproofing Works - 10th & 11th Floor WIP Flat Flooring - 3F, 4F WIP T. Dado - 2nd Floor Completed, 3rd & 4th WIP K. Platform - 6th Floor Completed, 7th & 8th WIP
SIERRA	TOWER 5	24th Floor Slab (28th Slab) - WIP 23rd Floor Slab (27th Slab) - RCC Completed Gypsum Works - 10th & 11th Floor WIP Plumbing Works - 14th & 15th Floor WIP Firefighting - 8th & 9th floor WIP Waterproofing Works - 13th & 14th Floor WIP Flat Flooring Works - 2nd Floor Completed & 3rd Floor WIP T. Dado - 5th & 6th Floor WIP K. Platform - 5th & 6th Floor WIP
SIERRA	TOWER 6	24th Floor Slab (28th Slab) - RCC Completed. 25th Floor Slab (29th Slab) - RCC P1 completed and P2 WIP Gypsum Work - 17th & 18th Floor WIP Waterproofing & Plumbing Works - 17th & 18th Floor WIP Fire Fighting Works - 14th Floor WIP Tile Dado - 9th & 10th Floor WIP Kitchen Platform - 9th Floor WIP Flooring Works - 9th & 10th floor WIP



Tower 1 – RCC Completed.



Tower 01-02 : Night View.



Tower 1 – Finishing Work



Tower 2: RCC Completed.



Tower 2 – Finishing Work



Tower 3 Finishing Activities - WIP




Tower 3 – Finishing Work



Tower 4 – 22nd Floor Slab RCC Work – WIP.



Tower 4 – Finishing Work

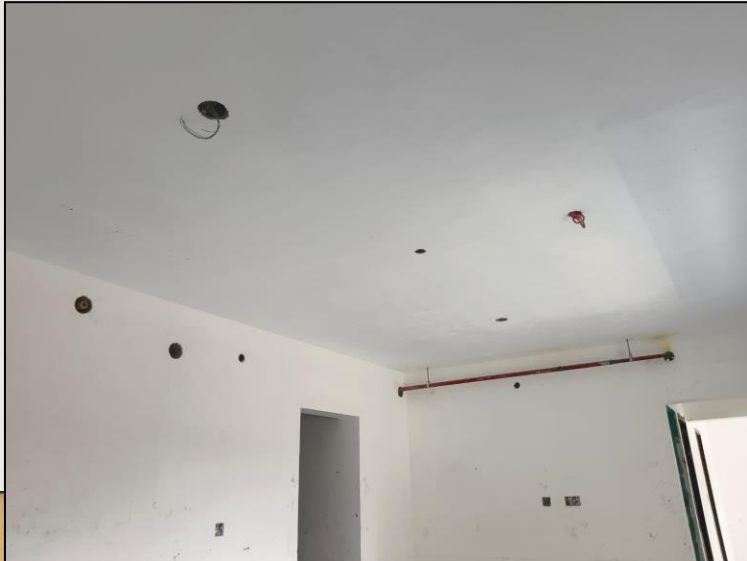

Tower 5 – 24th Floor Slab – RCC WIP.



Tower 5 – Finishing Work



Tower 6 – 25th Floor Slab - RCC P2 completed & P1 WIP Central Podium – 5th Slab Work Completed



Tower 06

Central Podium

Tower 6 – Finishing Work

