

VTP SIERRA PROJECT

Site Progress report

REPORT DATE: 05-07-2025


Building Work Status

Project / Township	Tower	Construction Status as on 04.07.2025
SIERRA	TOWER 1	Tower 01 : RCC Completed Gypsum Work - Completed. Waterproofing & Plumbing Work - Completed Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed Flooring Works - Completed Wooden Door - Completed, Accessories installation WIP Aluminium Works (Window & Door) - WIP External Painting Work in progress Internal Painting Works - WIP (1st Coat Paint)
SIERRA	TOWER 2	Tower 02 : RCC Completed. Gypsum Work - Completed. Waterproofing & Plumbing - Completed. Fire Fighting Work - Completed. Tiling Works (Toilet Dado) - Completed. Flooring Works - Completed. Wooden Door - 13th To 25th Floor WIP Aluminium Works (Window & Door) WIP External Painting Work in progress Internal Painting Works - 9th Floor WIP (1st coat) Lift Installation Work in Progress
SIERRA	TOWER 3	Above Terrace Activities - Completed Waterproofing & Plumbing Work - 25th & 26 Floor WIP Fire Fighting Works - 26th Floor WIP. Tiling Works (Toilet Dado) - 21st & 22th Floor Work in Progress Flooring Works – 13 & 14th Floor WIP
SIERRA	TOWER 4	14th Floor Slab (18th Slab) RCC Work - RCC casting completed 15th Floor Slab (19th Slab) RCC Work – P1 completed, P2 WIP Gypsum Works - 5th Floor WIP. Waterproofing Works - 5th Floor WIP
SIERRA	TOWER 5	16th Floor Slab (20th Slab) - RCC casting completed 17th Floor Slab (21st Slab) - RCC WIP Plumbing Works - 3rd and 4th Floor WIP Waterproofing Works - 2nd and 3rd Floor WIP
SIERRA	TOWER 6	20th Floor Slab (24th Slab) - RCC Casting Completed 21st Floor Slab (25th Slab) - WIP Gypsum Work - 10th & 11th Floor WIP Waterproofing & Plumbing Works - 12th & 13th Floor WIP Fire Fighting Works - 10th & 11th Floor WIP Tile Dado - 5th & 6th Floor WIP Kitchen Platform - 5rd Floor WIP

Tower 1 – RCC Completed.




Tower 1 – Finishing Work

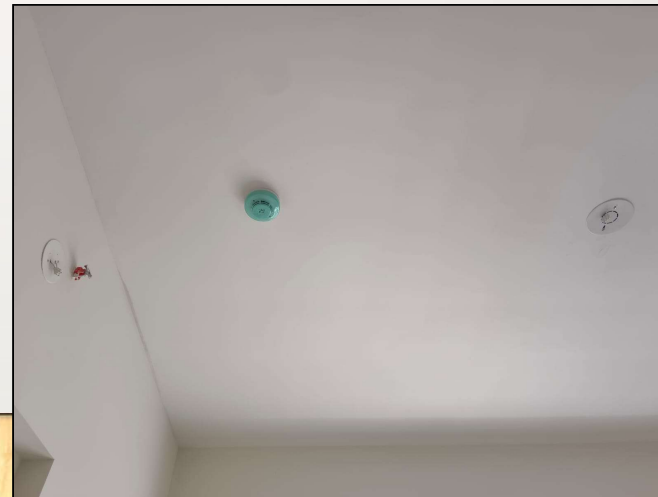

Tower 2: RCC Completed.



Tower 2 – Finishing Work

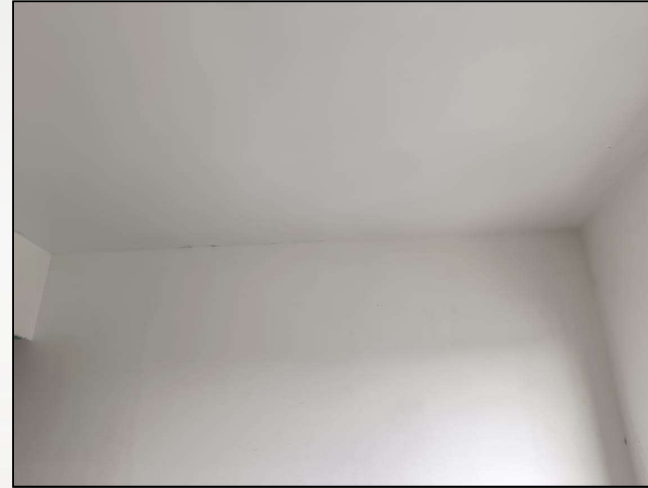

Tower 3 - Above Terrace RCC & Finishing Activities - WIP



Tower 3 – Finishing Work



Tower 4 – 15th Floor Slab RCC Work – P1 Completed & P2 WIP.



Tower 5 – 17th Floor Slab – RCC WIP.



Tower 6 – 21st Floor Slab - RCC WIP

Central Podium – 5th Slab Work Completed



Tower 06

Central Podium

Tower 6 – Finishing Work

